



SR 132 WEST


**State Route 99 / State Route 132 Interchange  
State Route 132 West – Gates to Dakota  
Delivery Update  
February 19, 2025**





# SR 132 West Needham Street to Gates Road

SR 132 WEST

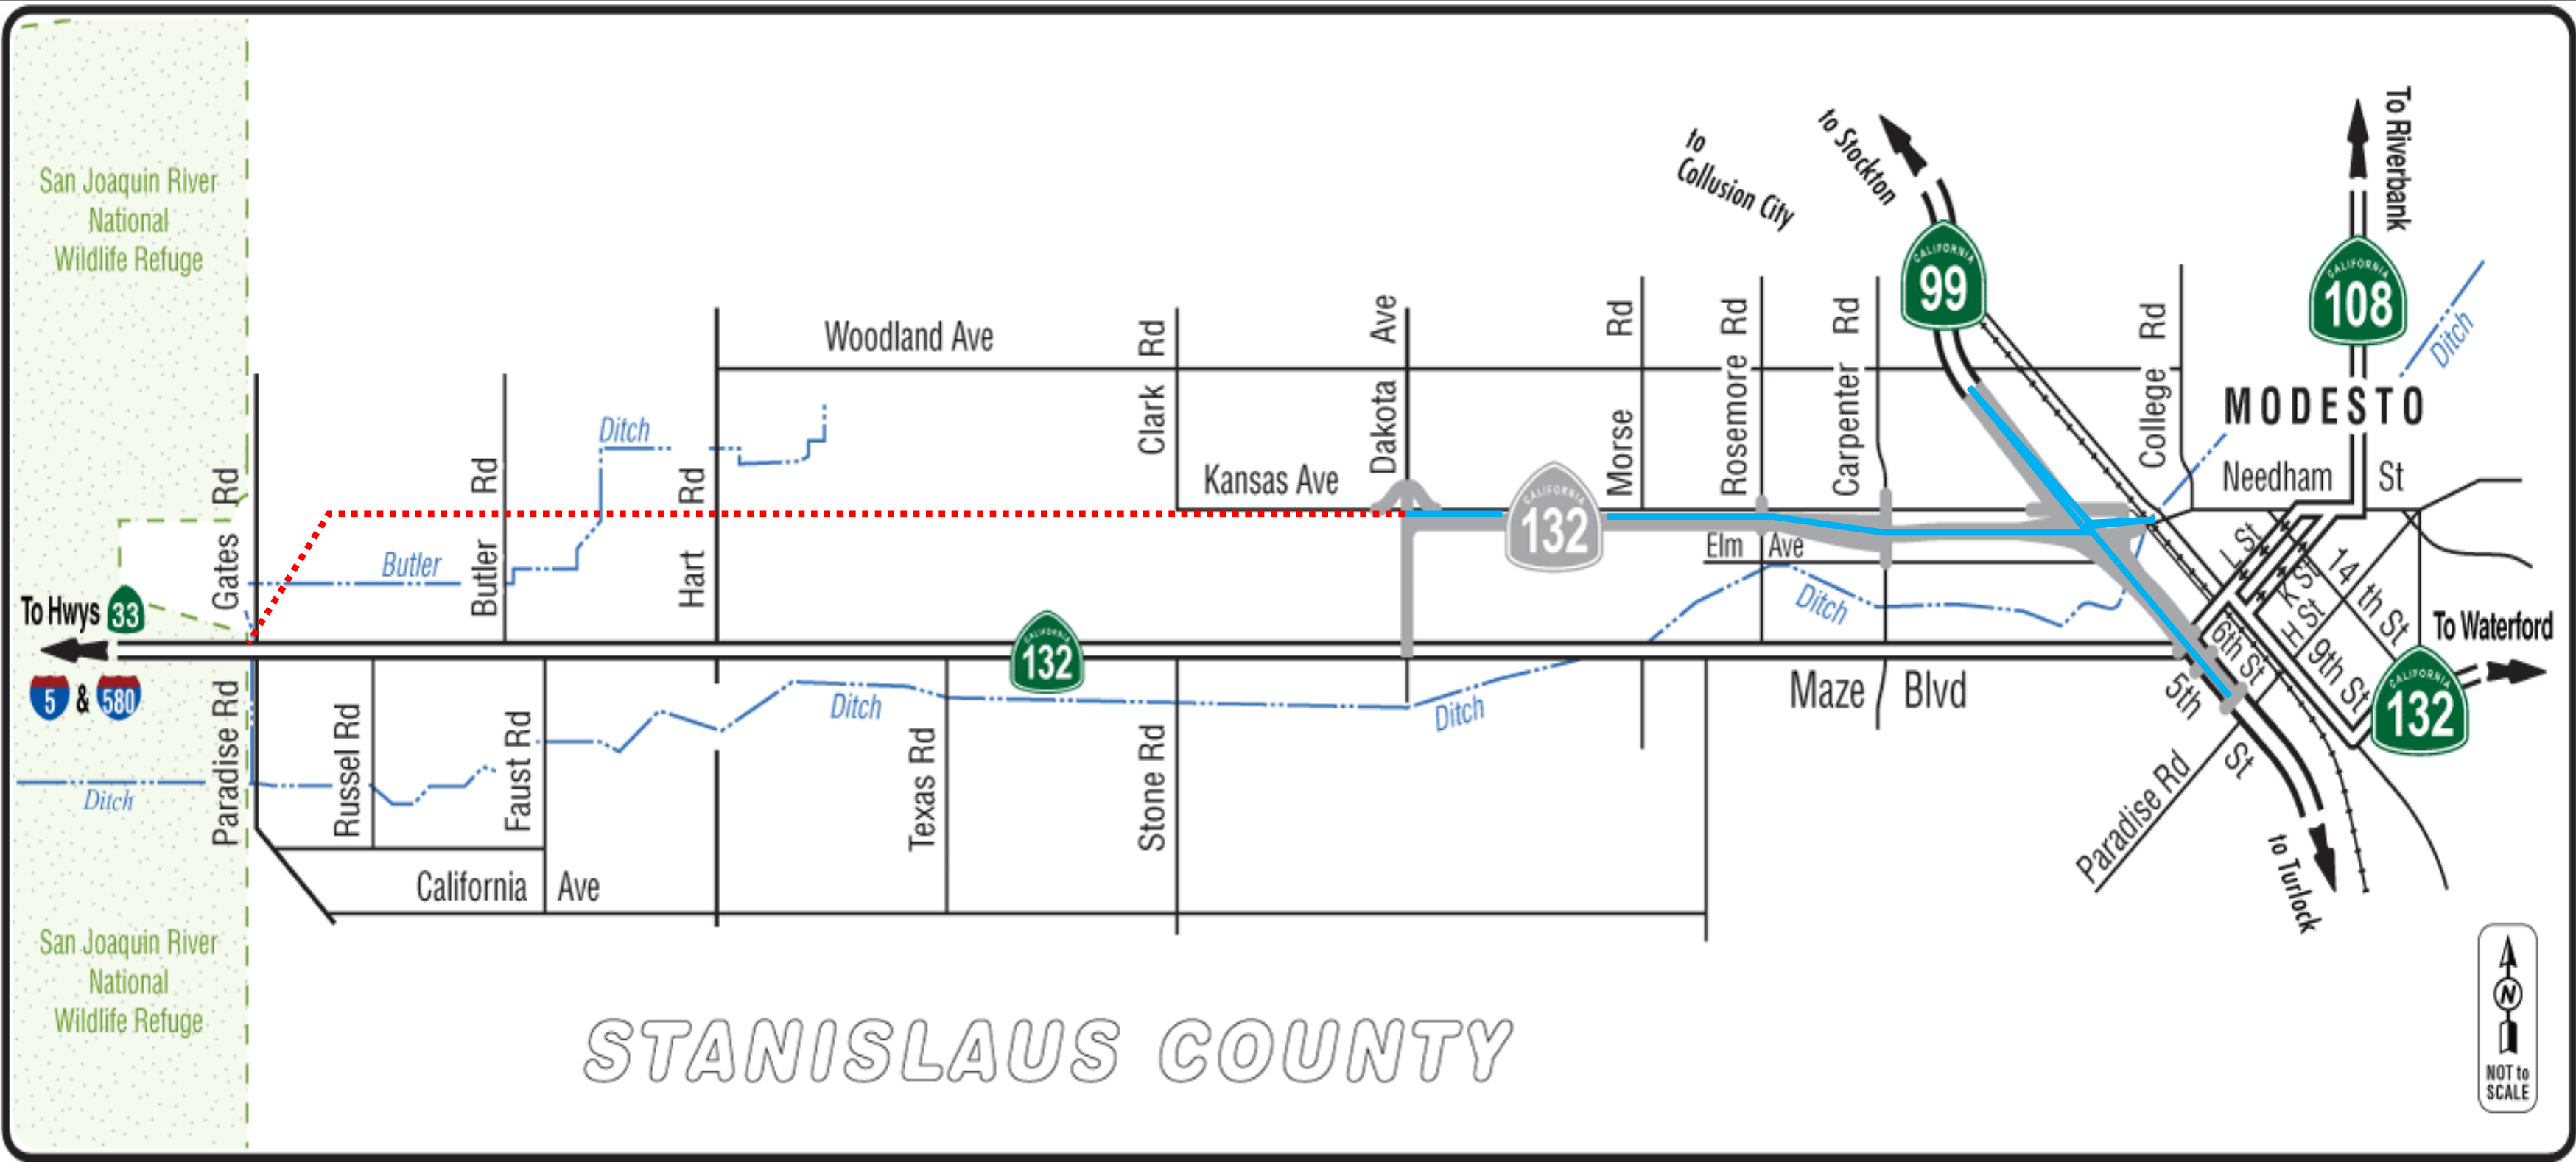



SR 132 WEST



SR 132 WEST

DAKOTA TO SR 99



SR 132 WEST

SR 99/SR 132 INTERCHANGE



SR 132 WEST

GATES TO DAKOTA



SR 132 WEST

GATES TO SR 99


# GATES Rd to DAKOTA Ave

- Two-lane Expressway
- Hart Road & Dakota Avenue Overcrossings
- Gates Road Roundabout



## SR 132 WEST

GATES TO DAKOTA

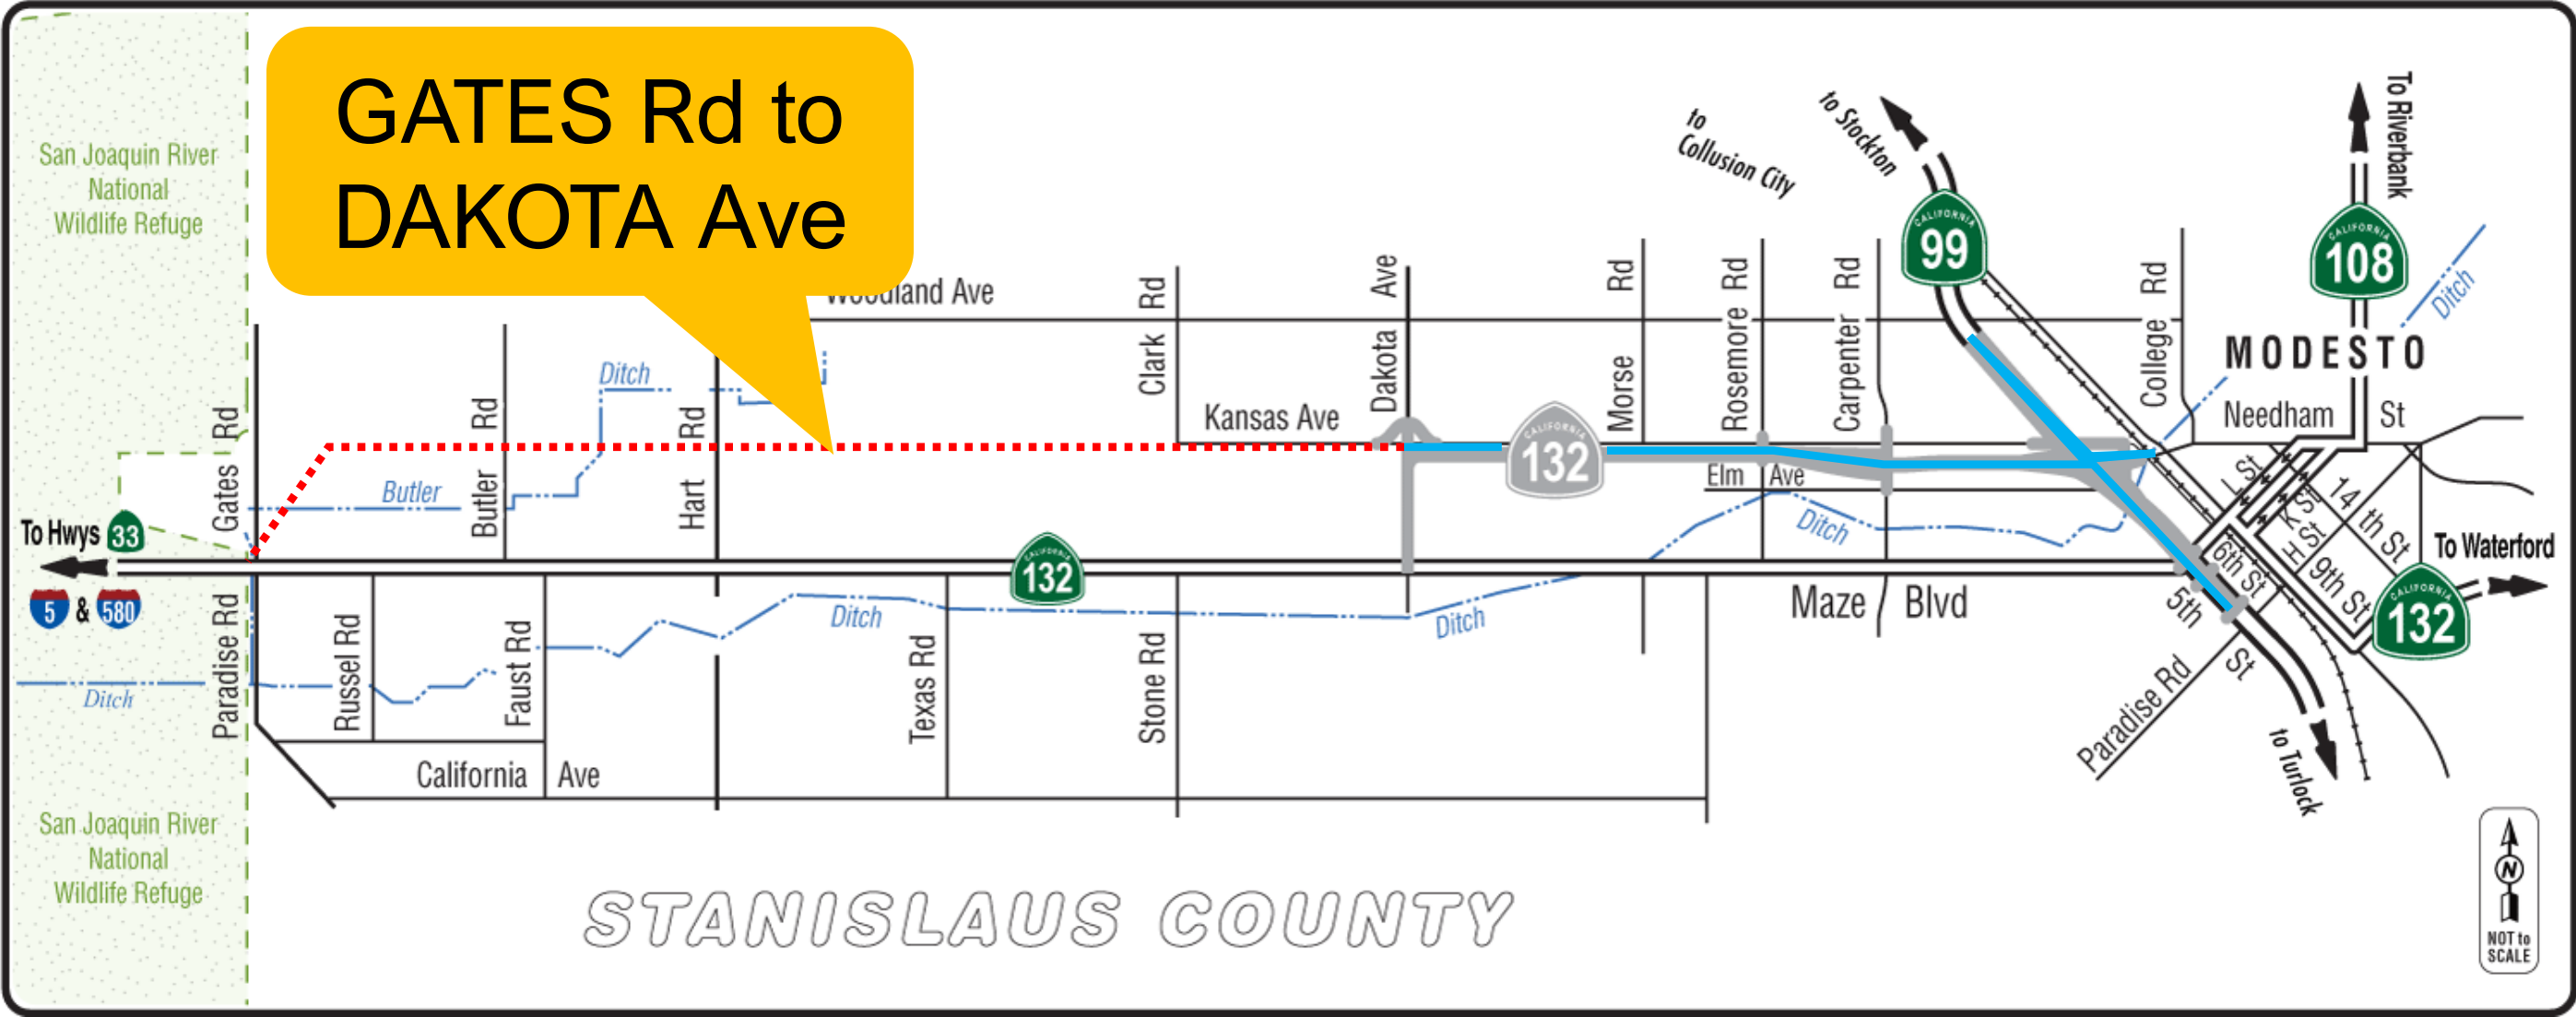




# SR 99 / SR 132 INTERCHANGE

- Freeway to Freeway Connection
- Kansas Avenue Interchange Improvements




## SR 132 WEST

SR 99/SR 132 INTERCHANGE

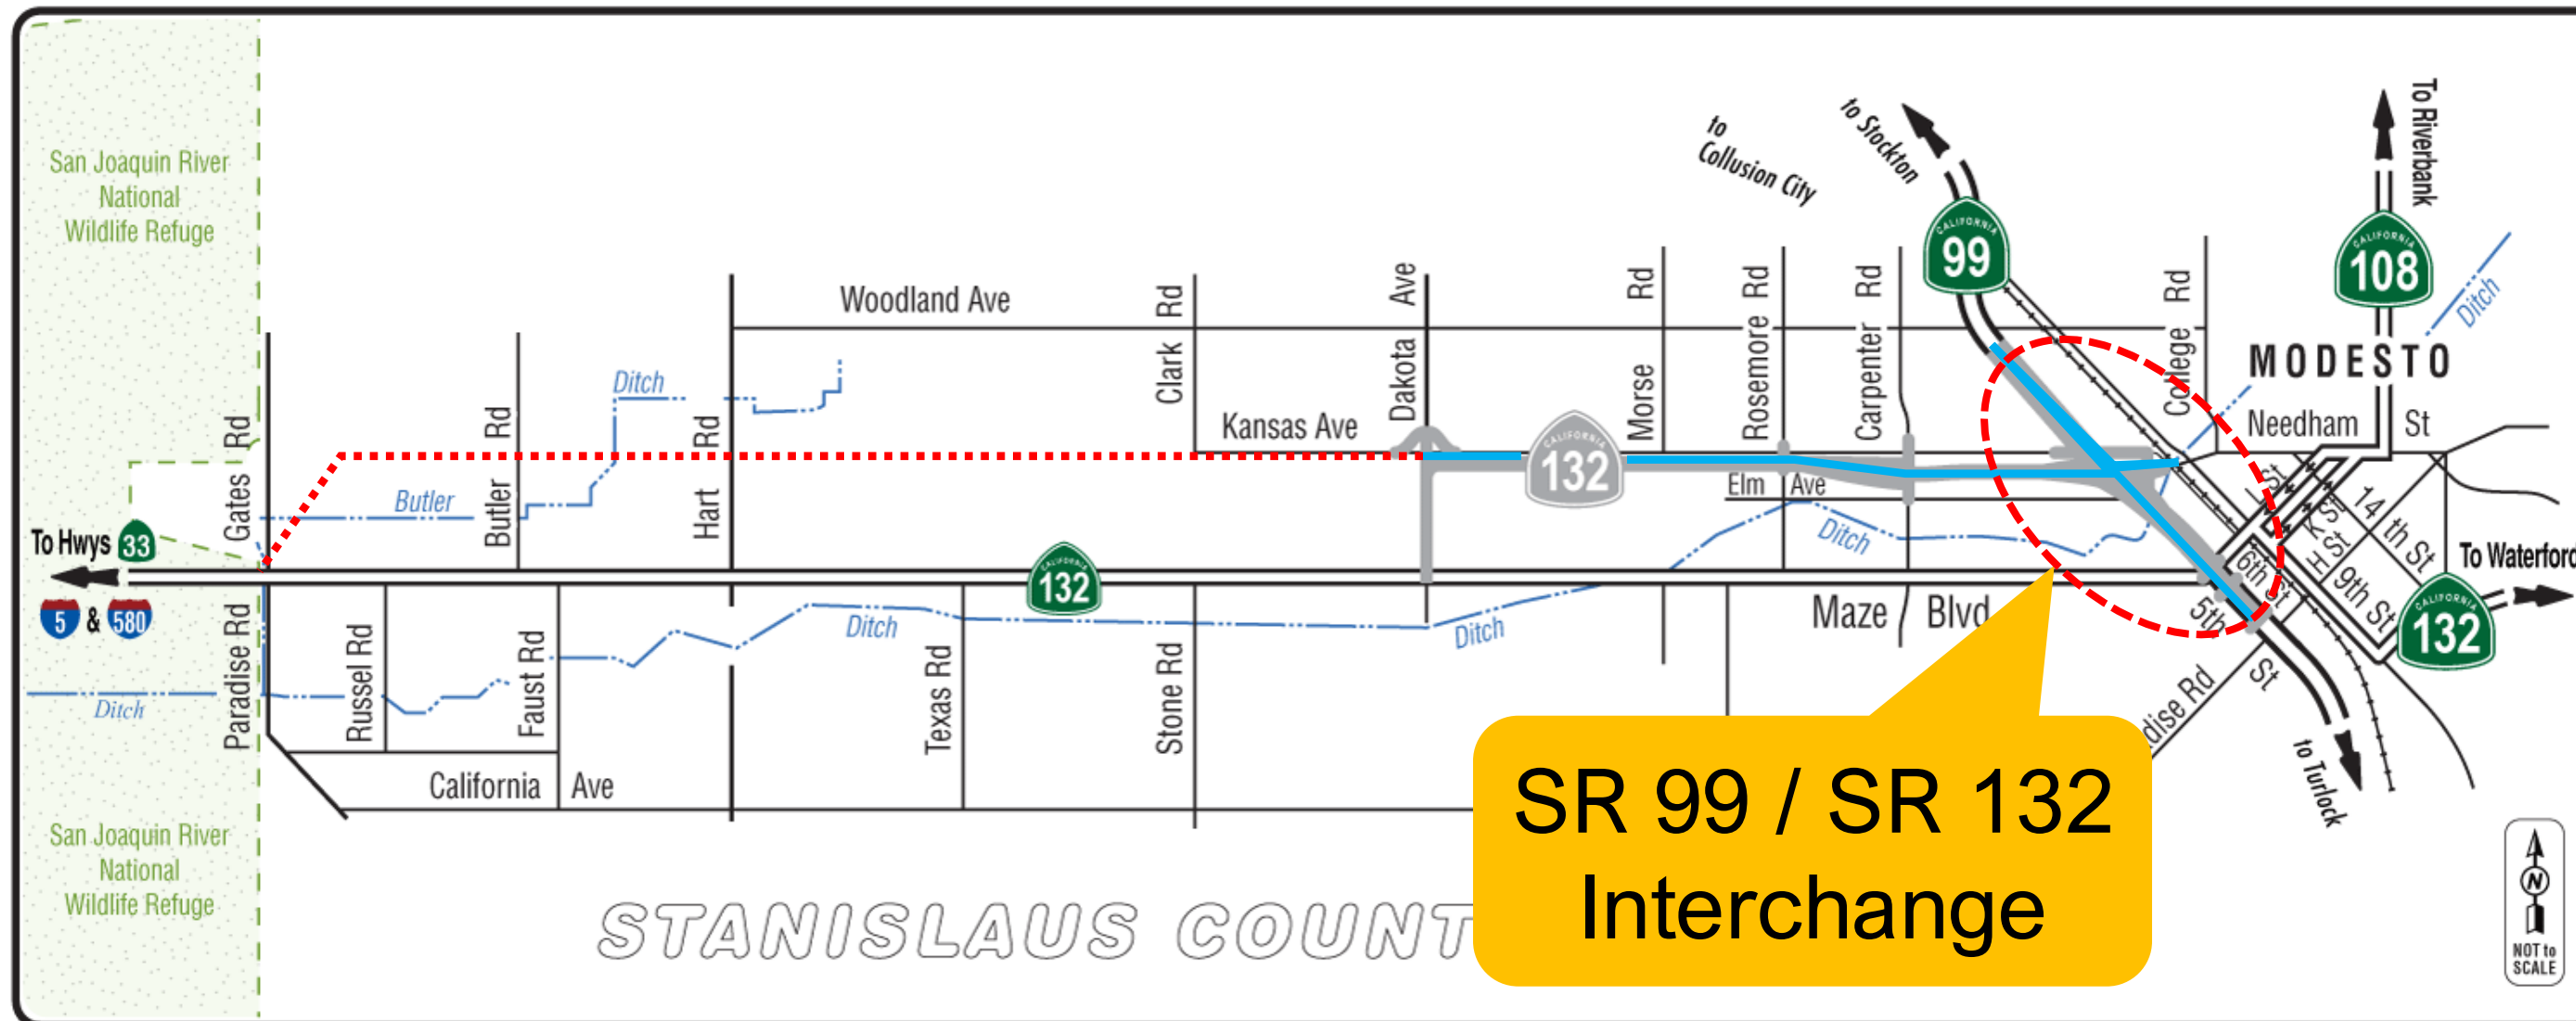

SR 99 / SR 132  
Interchange

# Where Are We Now?

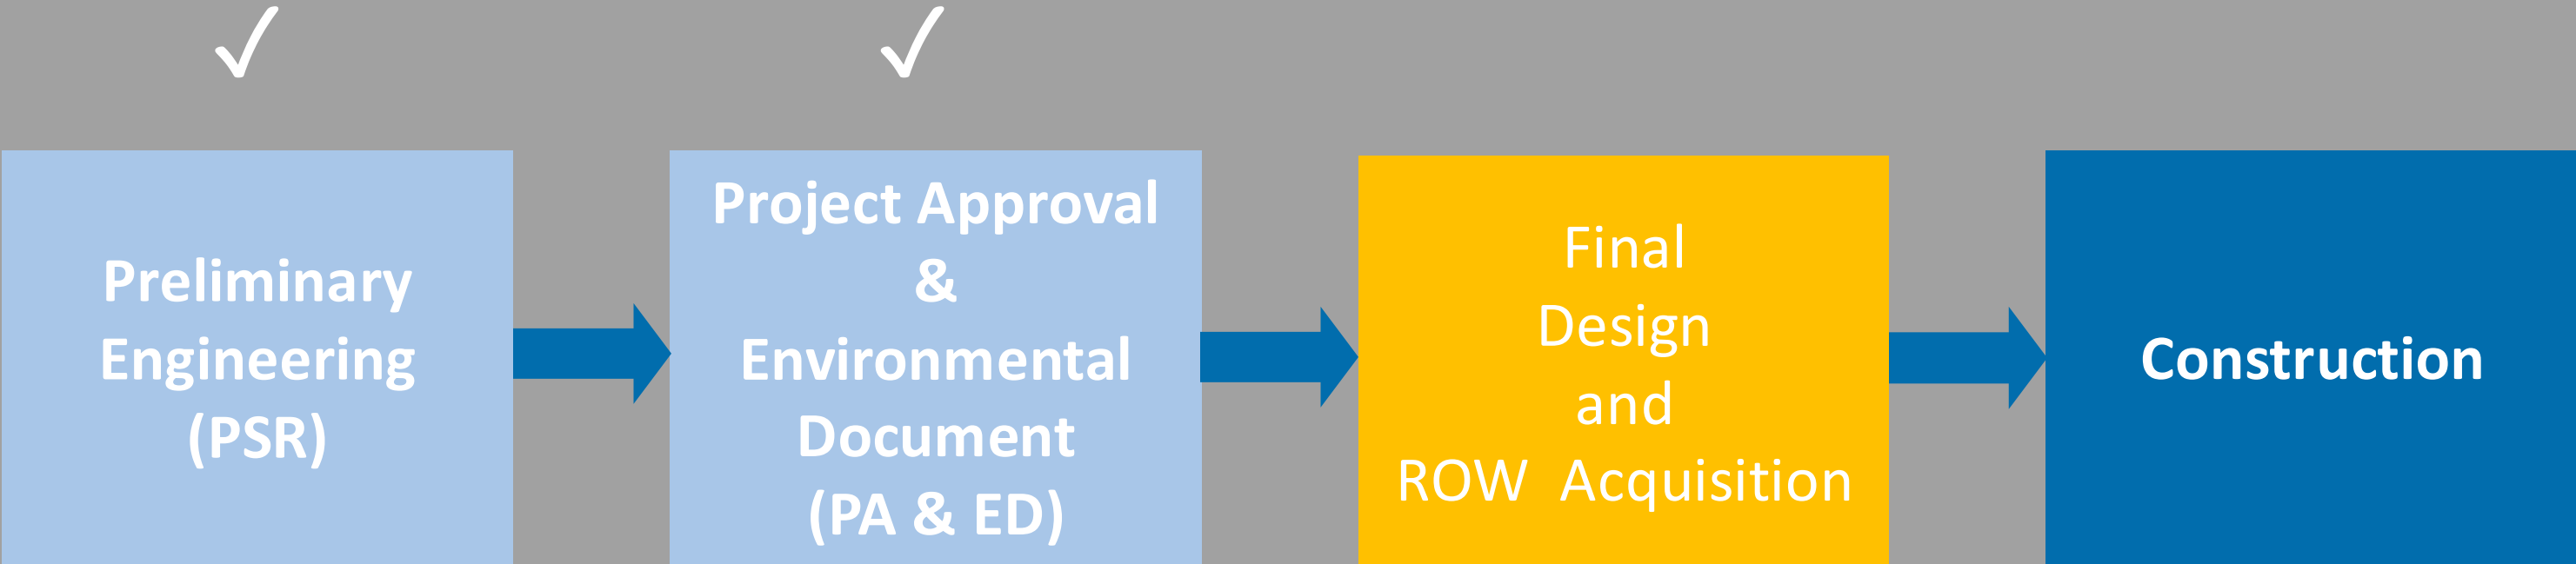




# Gates to Dakota Design Update



SR 132 WEST  
GATES TO DAKOTA

- 65% Plans, Specifications & Estimates submitted (January 2025)
- Modesto Irrigation District and Property Owners irrigation adjustments coordination

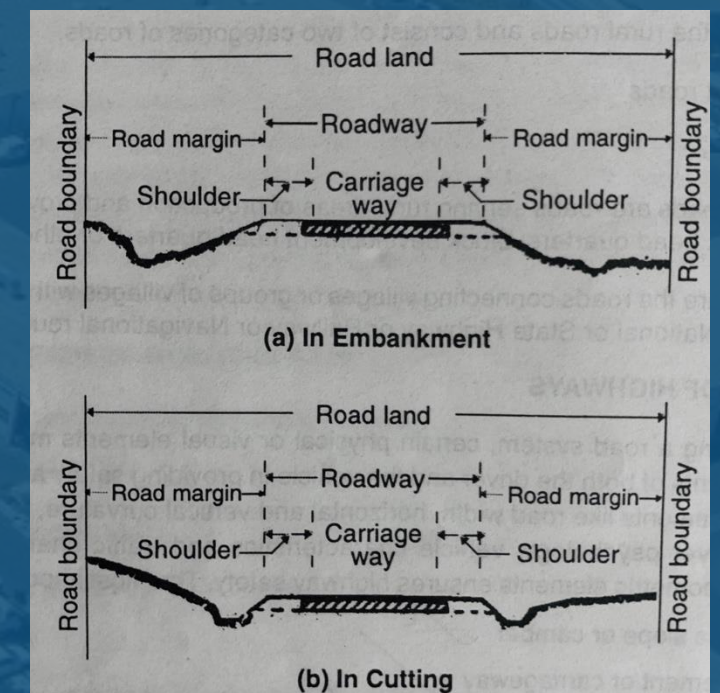




# SR 99 / SR 132 Interchange Design Update



SR 132 WEST

SR 99/SR 132 INTERCHANGE

- 95% Plans, Specifications & Estimates submittal - (April 2025)
- City of Modesto Corporation Yard impact coordination
- Drainage Basins / Pump Stations access & design coordination

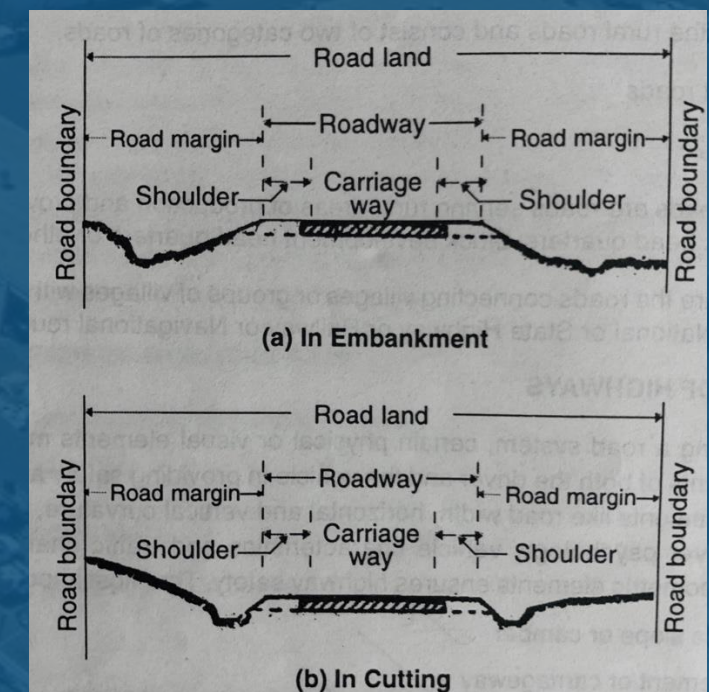



# Gates to Dakota


## Right of Way Acquisition Update



SR 132 WEST

GATES TO DAKOTA

- Acquisitions Statistics:
  - 22 Acquisitions Needed
  - 22 Appraisals Inspections Completed
  - 8 Appraisals Completed
  - Start Presenting Offers – March 2025
- Relocation Statistics:
  - 3 Residential Relocations Needed
  - No Business Relocations Needed

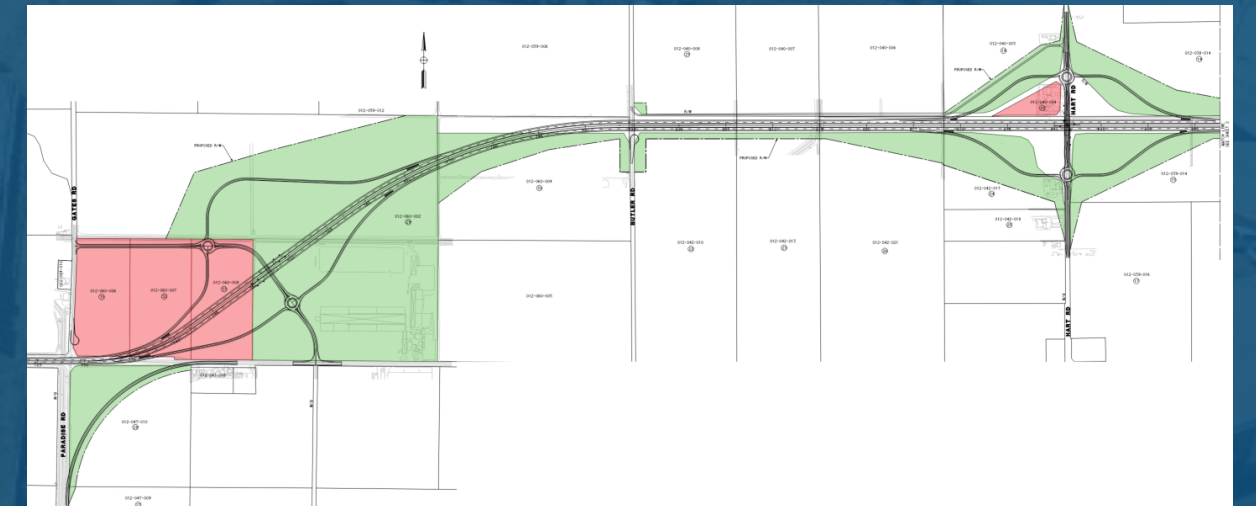



# SR 99 / SR 132 Interchange


## Right of Way Acquisition Update



SR 132 WEST

SR 99/SR 132 INTERCHANGE

- Acquisitions Statistics:
  - 44 Acquisitions Needed
  - 44 Appraisals Inspections Completed
  - 14 Appraisals Completed
  - 5 Offers Presented to Property Owners
- Relocation Statistics:
  - 24 Residential Relocations Needed
  - 4 Business Relocations Needed

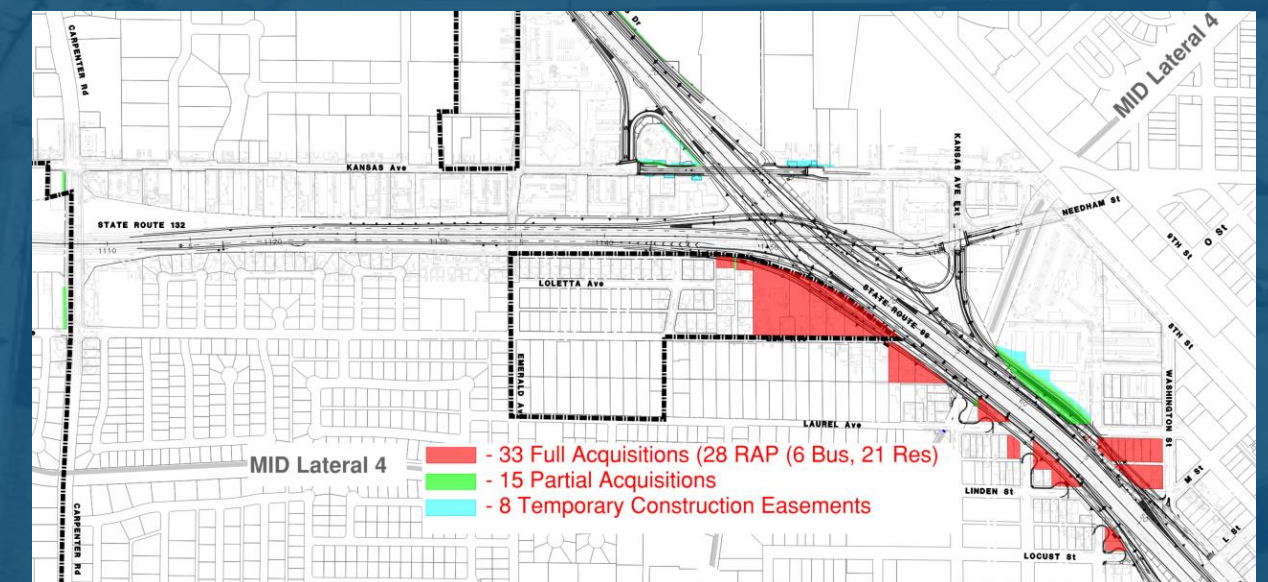



# Community Engagement Update



SR 132 WEST

- Local Organizations and Businesses outreach & follow up
- Media / News coverage monitoring
- Website and fact sheets updates
- Social Media information development & posting
- Community events / Presentations opportunities monitoring
- Project Inquiries responses





# Project Schedule

## SR 132 West – Gates to Dakota

- Right of Way Certification      October 2025
- Ready to List                      November 2025
- Begin Construction              April 2026
- End Construction                October 2028

## SR 99 / SR 132 Interchange

- Right of Way Certification      March 2026
- Ready to List                      April 2026
- Begin Construction              July 2026
- End Construction                October 2029





# Gates to Dakota Construction Funding



SR 132 WEST  
GATES TO DAKOTA

- **Estimated Construction Cost: \$77 million**
- **Funding Status:**
  - **TCEP application submitted; CTC decision- June 2025**
  - **Measure L**





# SR 99 / SR 132 Interchange Construction Funding



SR 132 WEST

SR 99/SR 132 INTERCHANGE

- Estimated Construction Cost: \$256 million
- Potential Funding Sources (Federal, State, Measure L)
- Federal BUILD application submitted





# PROJECT INFORMATION



SR 132 WEST



SR 132 WEST

HOME

ABOUT

PROJECT  
UPDATES

STAY  
INFORMED

COMMUNITY  
ENGAGEMENT



Website: <http://SR132West.com/>

Email: [contact@SR132West.com](mailto:contact@SR132West.com)





SR 132 WEST

Q & A
