




SR 132 WEST

**State Route 99 / State Route 132 Interchange
State Route 132 West – Gates to Dakota
Delivery Update
August 20, 2025**



SR 132 West Needham Street to Gates Road

SR 132 WEST

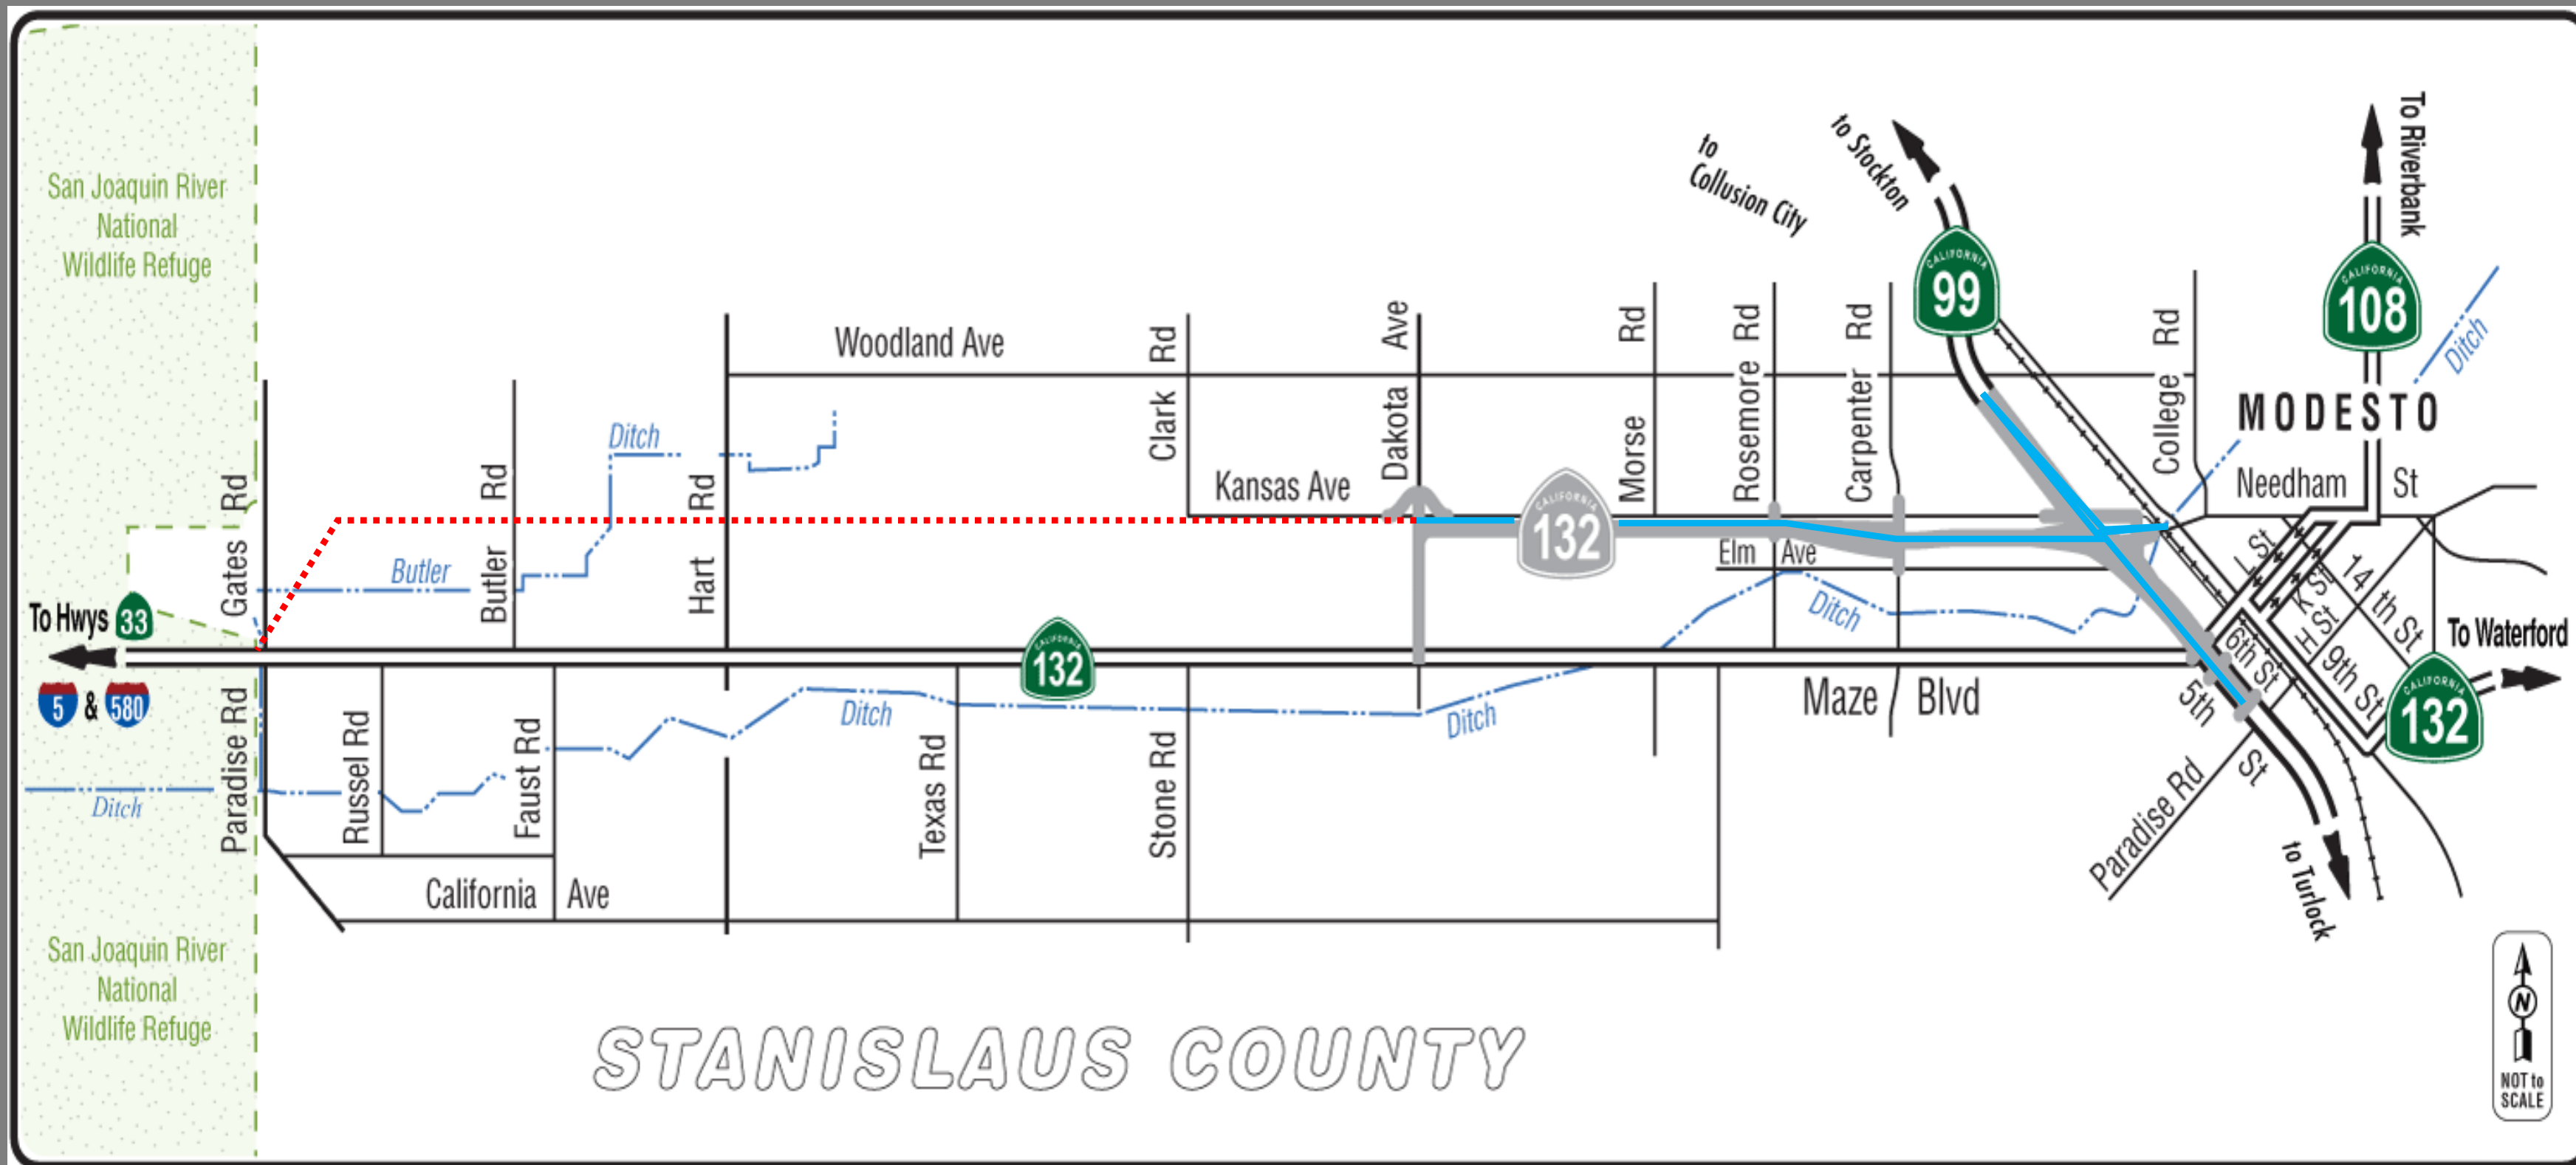

STANISLAUS COUNTY

COMPLETED

DESIGN / PERMITTING / RIGHT OF WAY



SR 132 WEST



SR 132 WEST

DAKOTA TO SR 99

DESIGN / PERMITTING / RIGHT OF WAY




SR 132 WEST

SR 99/SR 132 INTERCHANGE



SR 132 WEST

GATES TO DAKOTA



SR 132 WEST

GATES TO SR 99


GATES Rd to DAKOTA Ave

- Two-lane Expressway
- Hart Road & Dakota Avenue Overcrossings
- Gates Road Roundabout



SR 132 WEST

GATES TO DAKOTA

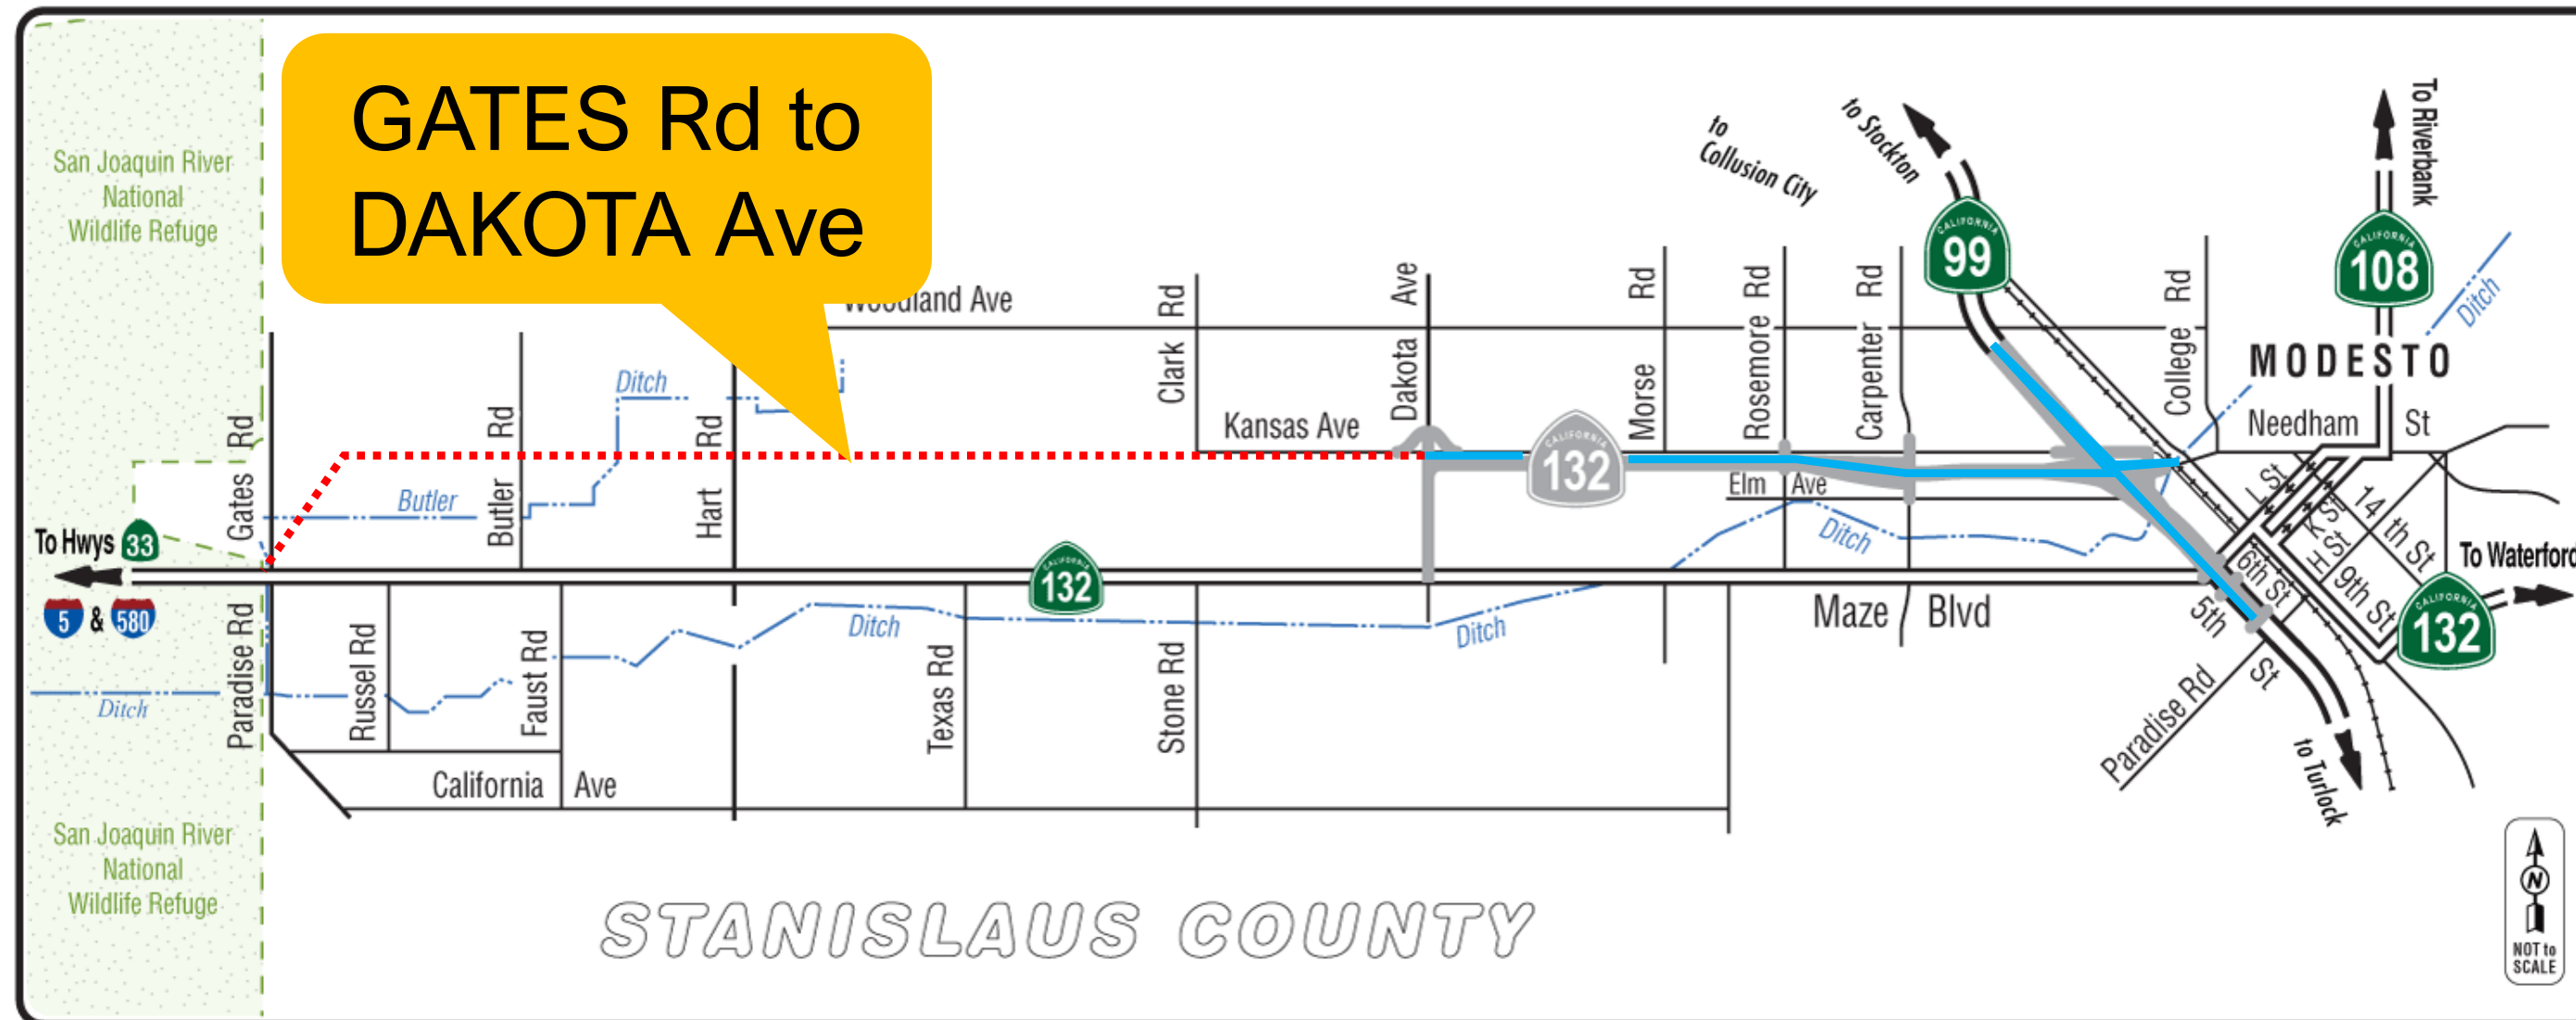


SR 99 / SR 132 INTERCHANGE

- Freeway to Freeway Connection
- Kansas Avenue Interchange Improvements




SR 132 WEST

SR 99/SR 132 INTERCHANGE

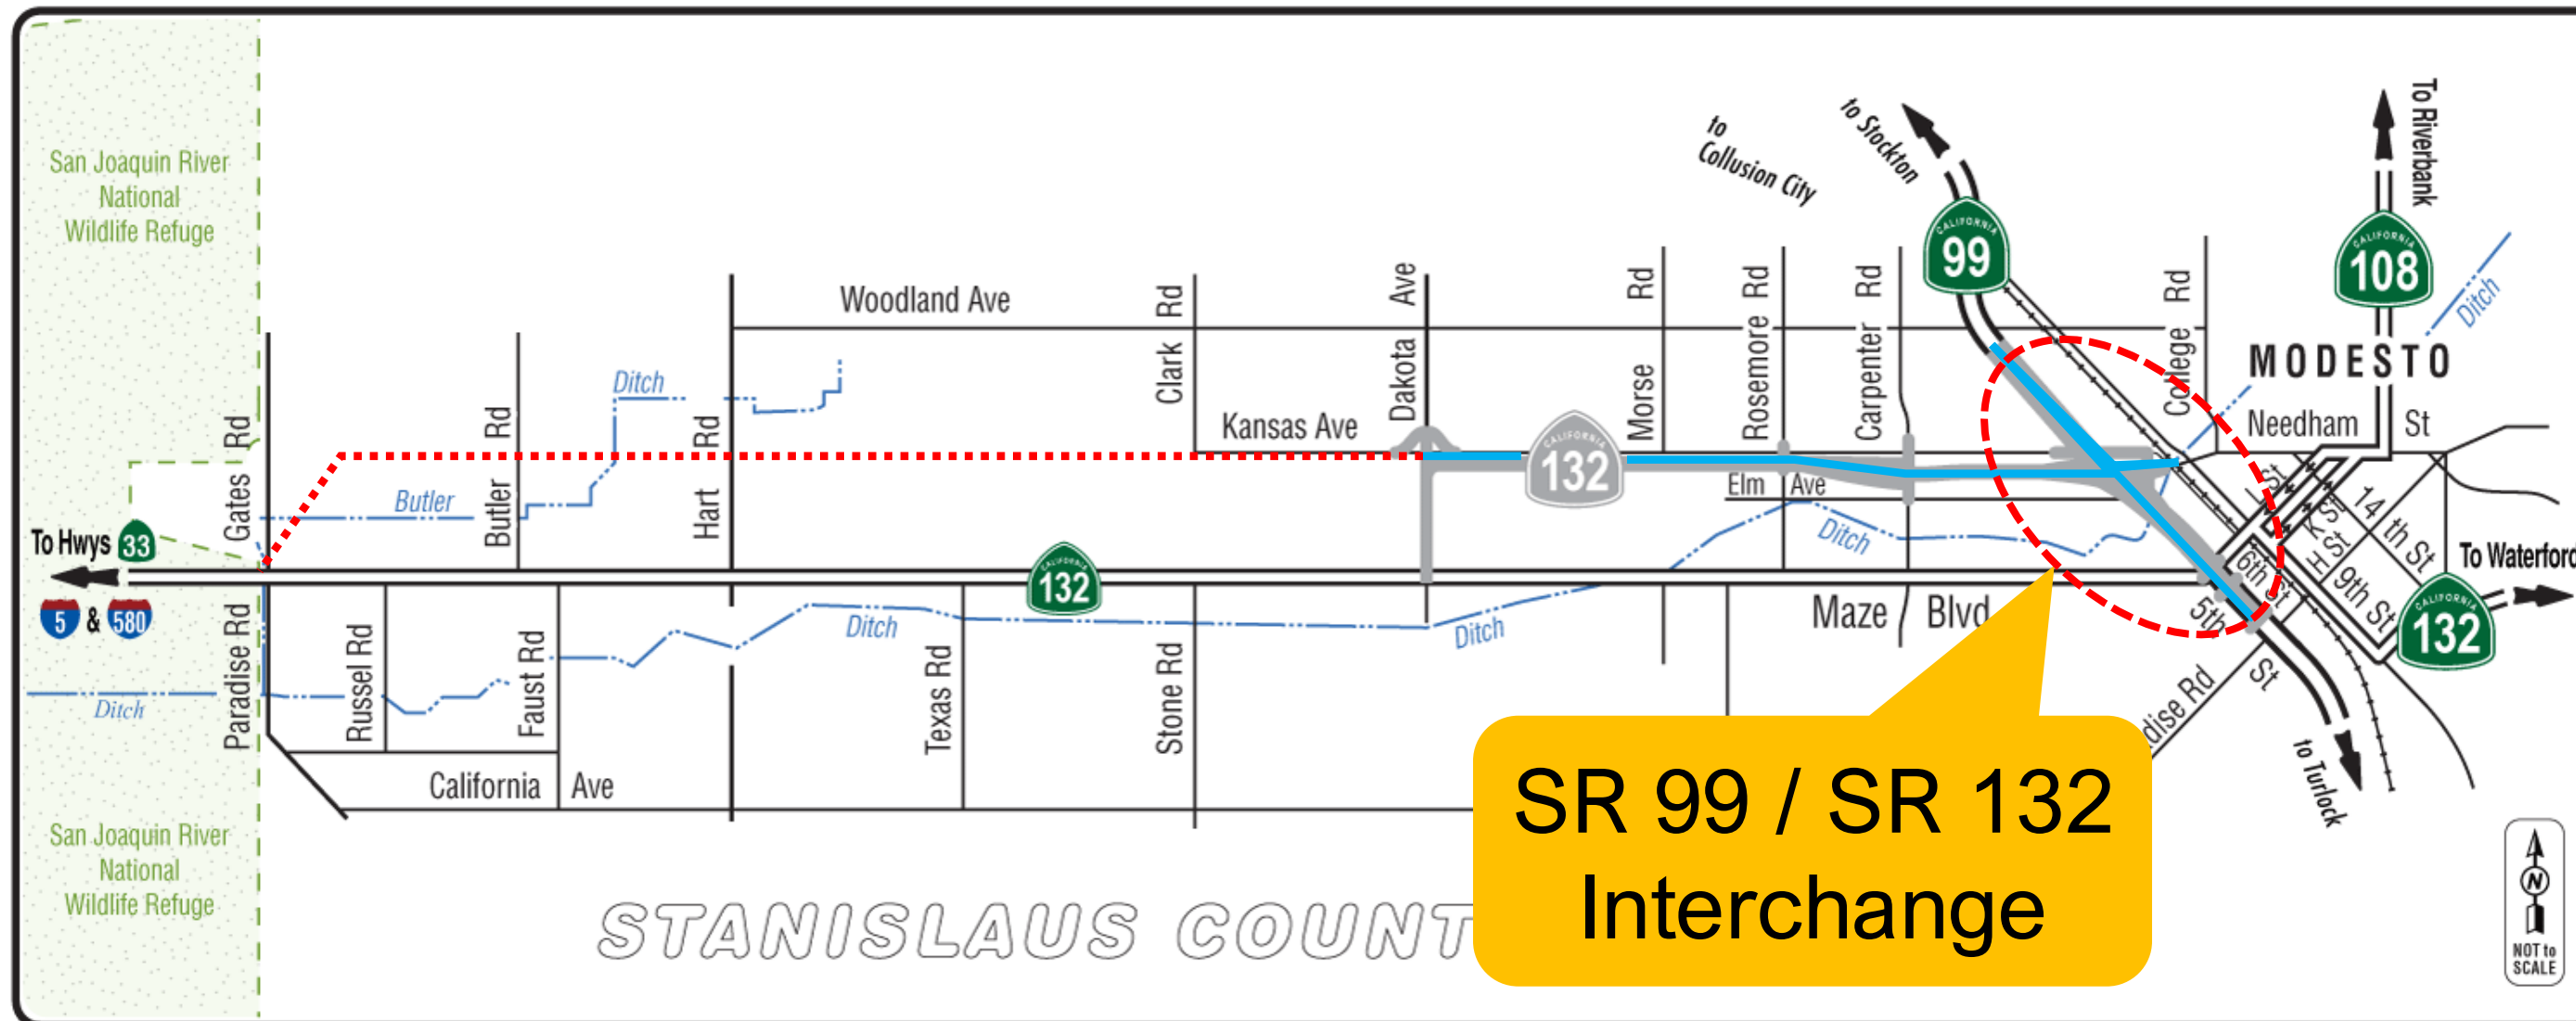

SR 99 / SR 132
Interchange

Where Are We Now?

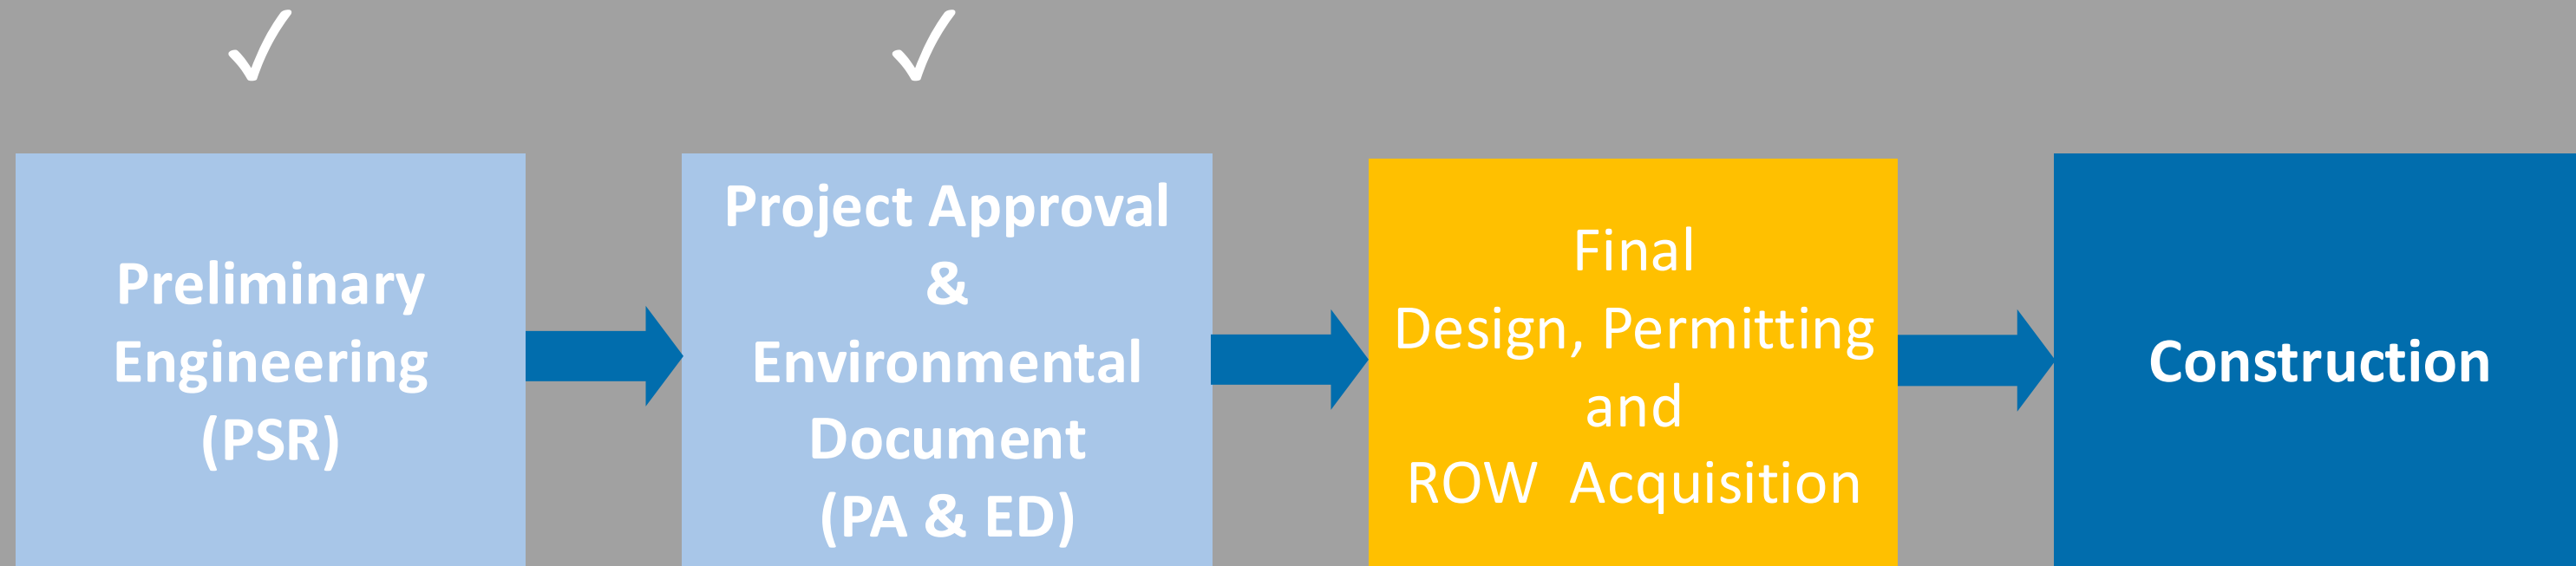


Gates to Dakota Design Update



SR 132 WEST

GATES TO DAKOTA

- 95% County / Caltrans Plans, Specifications & Estimates review completed (August 2025)
- 100% Plans, Specification & Estimate submittal (January 2026)
- Modesto Irrigation District and Property Owners irrigation adjustments coordination (On-going)

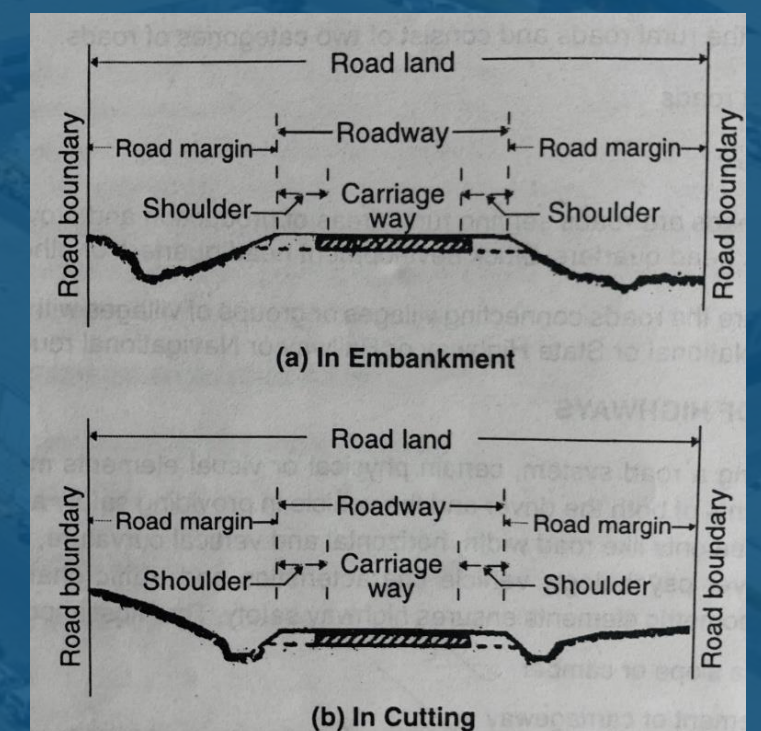


Gates to Dakota Permitting Update



SR 132 WEST
GATES TO DAKOTA

- Air Quality Conformity Report update (October 2025)
- Regional Water Quality Board Permit (October 2025)
- Modesto Irrigation District Agreements (October 2025)

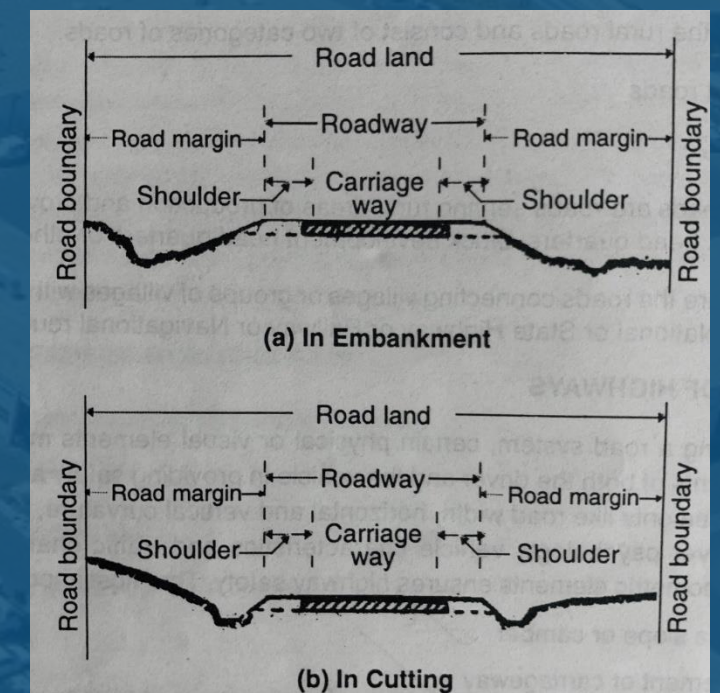


SR 99 / SR 132 Interchange Design Update



SR 132 WEST

SR 99/SR 132 INTERCHANGE

- 95% Plans, Specifications & Estimates submittal - (October 2025)
- City of Modesto Corporation Yard impact coordination
- Drainage Basins / Pump Stations access & design coordination
- Utility Relocation coordination

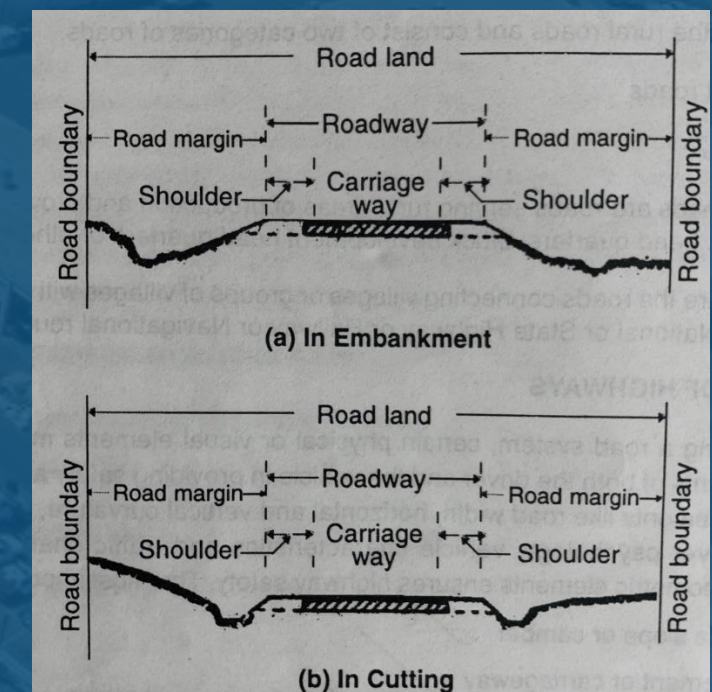


Gates to Dakota

Right of Way Acquisition Update



- Acquisition Statistics:
 - 22 Acquisitions Needed
 - 18 Appraisals Completed
 - 14 Offers Presented to Property Owners
 - 1 Agreement Reached
- Relocation Statistics:
 - 2 Residential Relocations Needed
 - 1 Business Relocation Needed

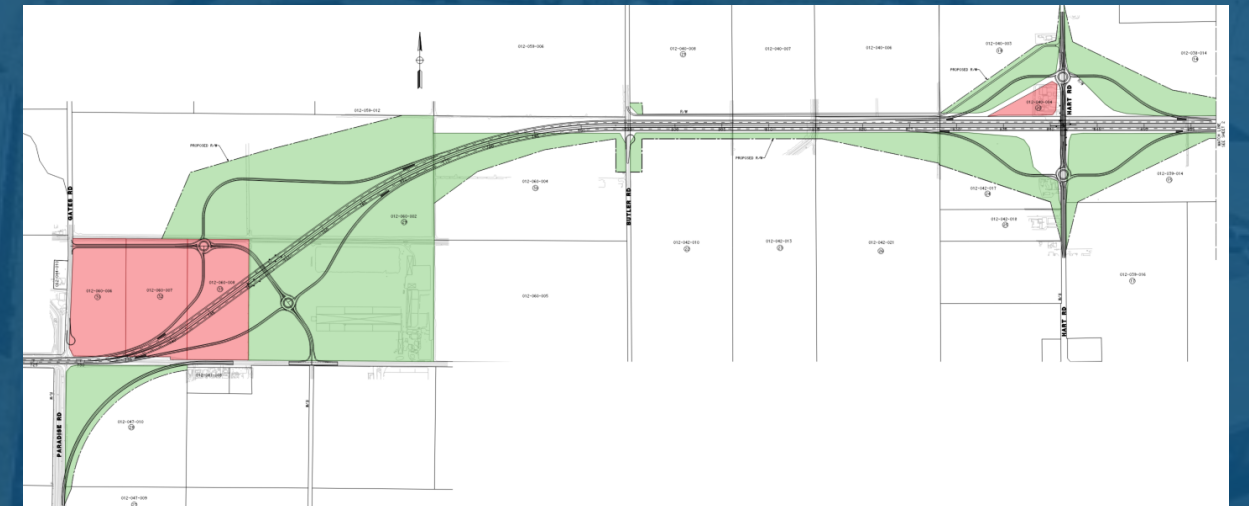


SR 99 / SR 132 Interchange

Right of Way Acquisition Update



SR 132 WEST
SR 99/SR 132 INTERCHANGE

- Acquisition Statistics:
 - 43 Acquisitions Needed
 - 32 Appraisals Completed
 - 16 Offers Presented to Property Owners
 - 7 Agreements reached with Owners
- Relocation Statistics:
 - 28 Residential Relocations Needed
 - 6 Business Relocations Needed

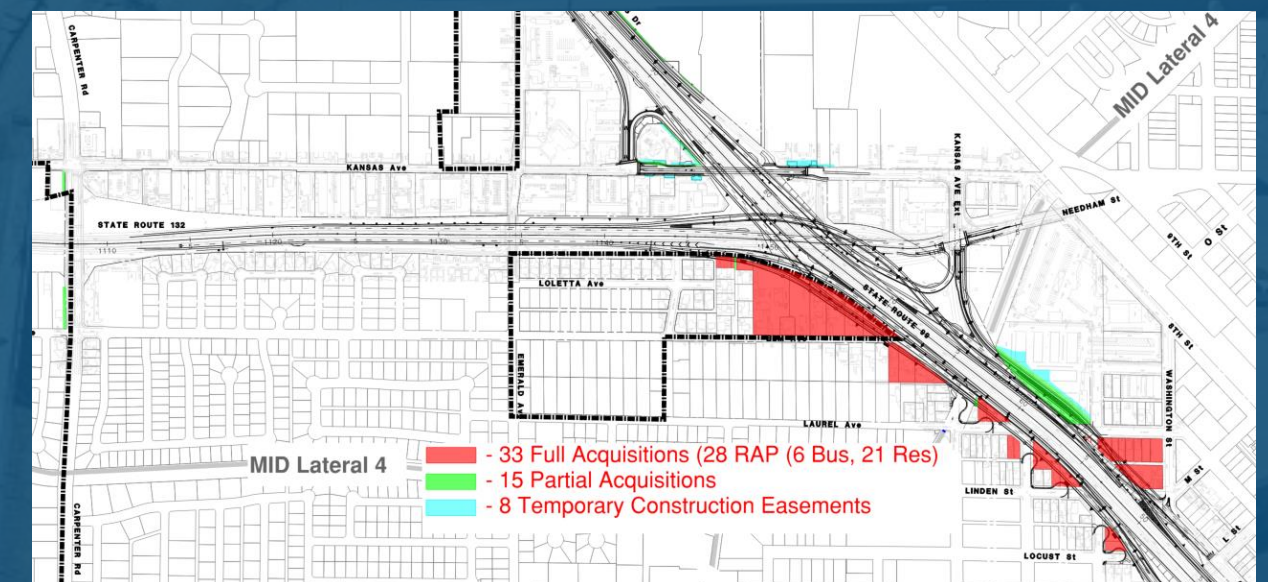

Community Engagement Update



SR 132 WEST

- Public Open House
 - Central Catholic High School (October 2, 2025, at 5:30 pm)
- Website and fact sheets updates
- Social Media information development & posting
- Community events / Presentation opportunities
 - Farm Bureau (March 10, 2025)
 - Modesto Earth Day (April 19, 2025)
 - Modesto Farmer's Market (June 12, 2025)
- Project Inquiries responses
- Project Newsletter



Project Schedule

SR 132 West – Gates to Dakota

- Ready to List March / April 2026
- CTC Const. Allocation May / June 2026
- Begin Construction December 2026
- End Construction Summer / Fall 2029

SR 99 / SR 132 Interchange

- Ready to List November 2026
- Begin Construction June 2027
- End Construction Summer / Fall 2030



Gates to Dakota Construction Funding



SR 132 WEST
GATES TO DAKOTA

- **Estimated Construction Cost: \$77 million**
- **Funding Status:**
 - **TCEP application approved \$67 million**
 - **2025 / 2026 Fiscal Year (CTC construction allocation before June 30, 2026)**
 - **Measure L \$10 million**



SR 99 / SR 132 Interchange Construction Funding



SR 132 WEST

SR 99/SR 132 INTERCHANGE

- **Estimated Construction Cost: \$256 million**
- **Potential Funding Sources (Federal, State, Measure L)**



Expressway Roundabout Example US 93 in Arizona



SR 132 WEST

GATES TO DAKOTA



Expressway Roundabout Example Flashing Beacon and Signage



SR 132 WEST
GATES TO DAKOTA



Next Steps



- Trade Corridor Enhancement Program baseline agreement (September 2025)
 - CTC, Caltrans & StanCOG approval required
 - Schedule commitment (CTC construction allocation before June 30, 2026)
 - Potential cost increase funding commitment
- SR 132 West Policy Board right of way process update (September 2025)
- Gates to Dakota right of way acquisition (Critical Path Item)
 - Ready to List (March / April 2026)
 - Resolution of Necessity Hearings & Adoptions (September / October 2025)
 - Right of way negotiations (on going)

Next Steps (cont.)



- **Gates to Dakota construction management consultant procurement**
- **Public Open House Meeting (October 2, 2025)**
- **SR 99 / SR 132 Interchange construction funding strategy**

PROJECT INFORMATION



SR 132 WEST



SR 132 WEST

HOME

ABOUT

PROJECT
UPDATES

STAY
INFORMED

COMMUNITY
ENGAGEMENT



Website: <http://SR132West.com/>

Email: contact@SR132West.com



SR 132 WEST

Q & A
